



Parks GO Bond Update

September 14, 2022



Existing Parks Improvement Projects Completed

- Horton Park
- Giuffrida Park
- Northwest Softball Complex
- Storm Football Complex
- Pelican Softball Complex
- Pelican Baseball Complex
- Koza/Saladino Park
- Strausser BMX Sports Complex

Cultural Park



**Contract Amount:
\$2,938,141**

**Construction:
95% Complete**

**Contractor:
Waypoint
Contracting, Inc.**



Gator Circle Park



**Contract Amount:
\$2,114,588**

**Construction:
95% Complete**

**Contractor:
Waypoint
Contracting, Inc.**



Giuffrida Park



**Contract Amount:
\$654,120**

**Construction:
Substantially
Complete**

**Contractor:
EnviroStruct, LLC**



Del Prado Linear Park



**Contract Amount:
\$1,341,220**

**Construction:
70% Complete**

**Contractor:
EnviroStruct, LLC**



Sands Park



**Contract Amount:
\$3,188,751**

**Construction:
60% Complete**

**Contractor:
Wright
Construction**




Coviello Park



**Contract
Amount:
\$1,996,981**

**Construction:
25% Complete**

**Contractor:
Wright
Construction**

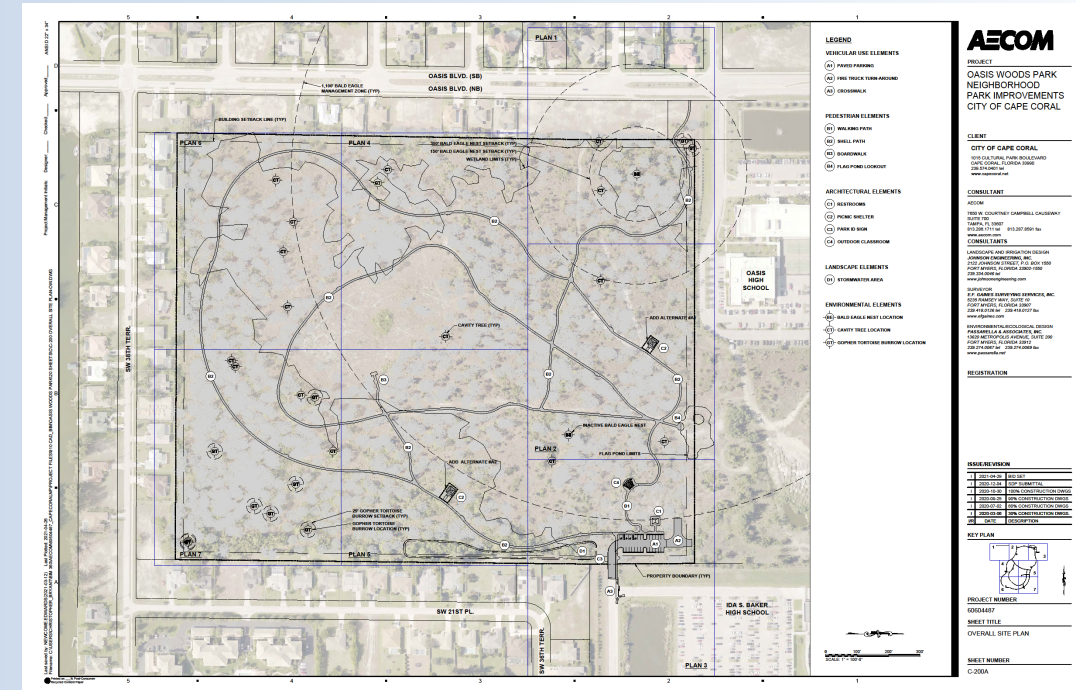


Contractor:
OAC Action Construction, Corp



Lake Kennedy Racquet Center

- **Contract Out to Bid**
- **Bid Opening:
September 2022**
- **Contract Duration:
Estimate 480 Days**

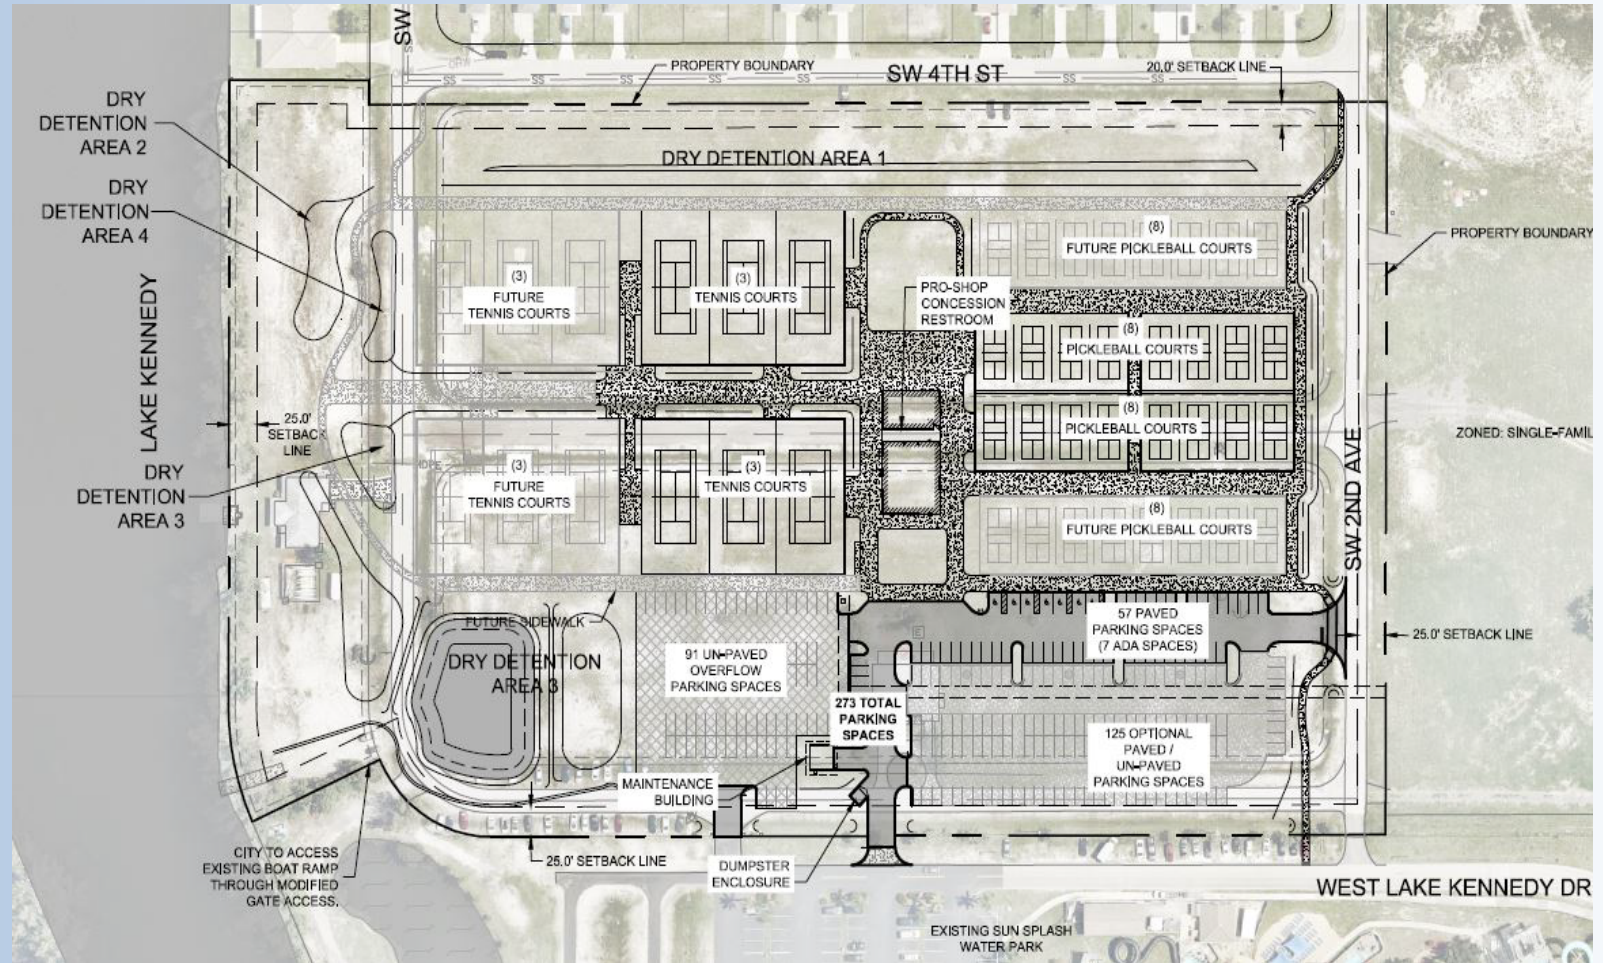


- **Contract to be Bid in Sept./Oct. 2022**
- **Contract Duration: Estimate 480 Days**



Tropicana Park

- Bid Package Prepared
- Waiting on ACOE and SFWMD Permits
- Contract Duration: Estimate 360 Days

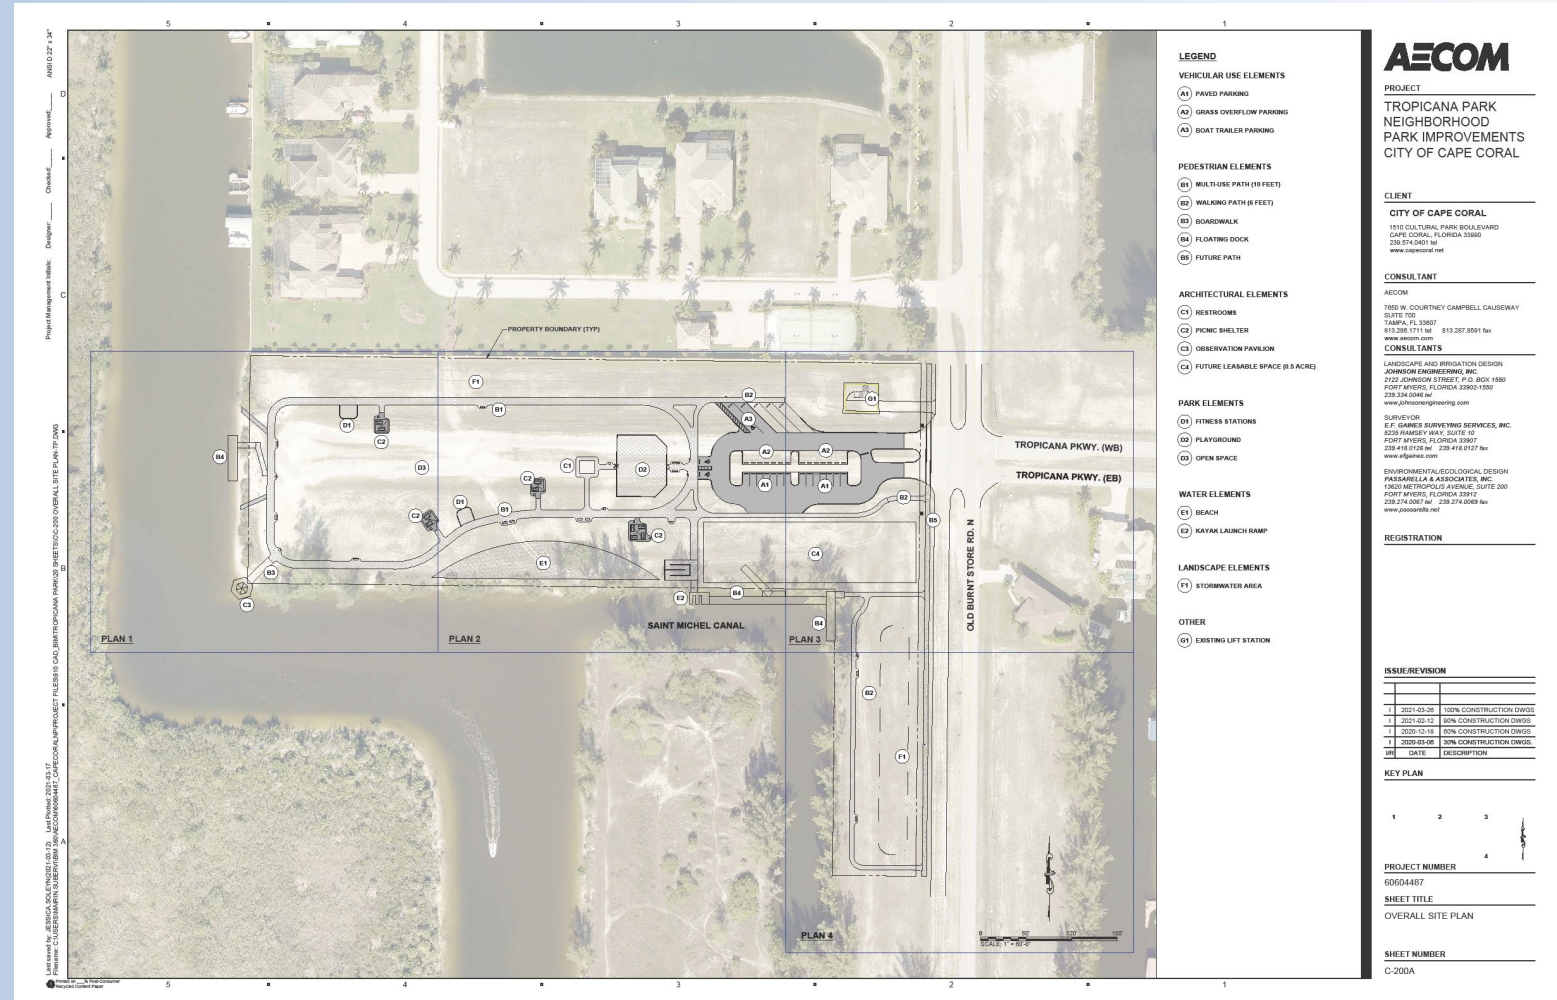


- **Bid Package Prepared**
- **Waiting on ACOE and SFWMD Permits**
- **Contract Duration:
Estimate 360 Days**



Lake Meade Park

- Bid Package Prepared
- SFWMD Permit received 5/13/22
- Waiting on DEP Permit
- Contract Duration: Estimate 360 Days

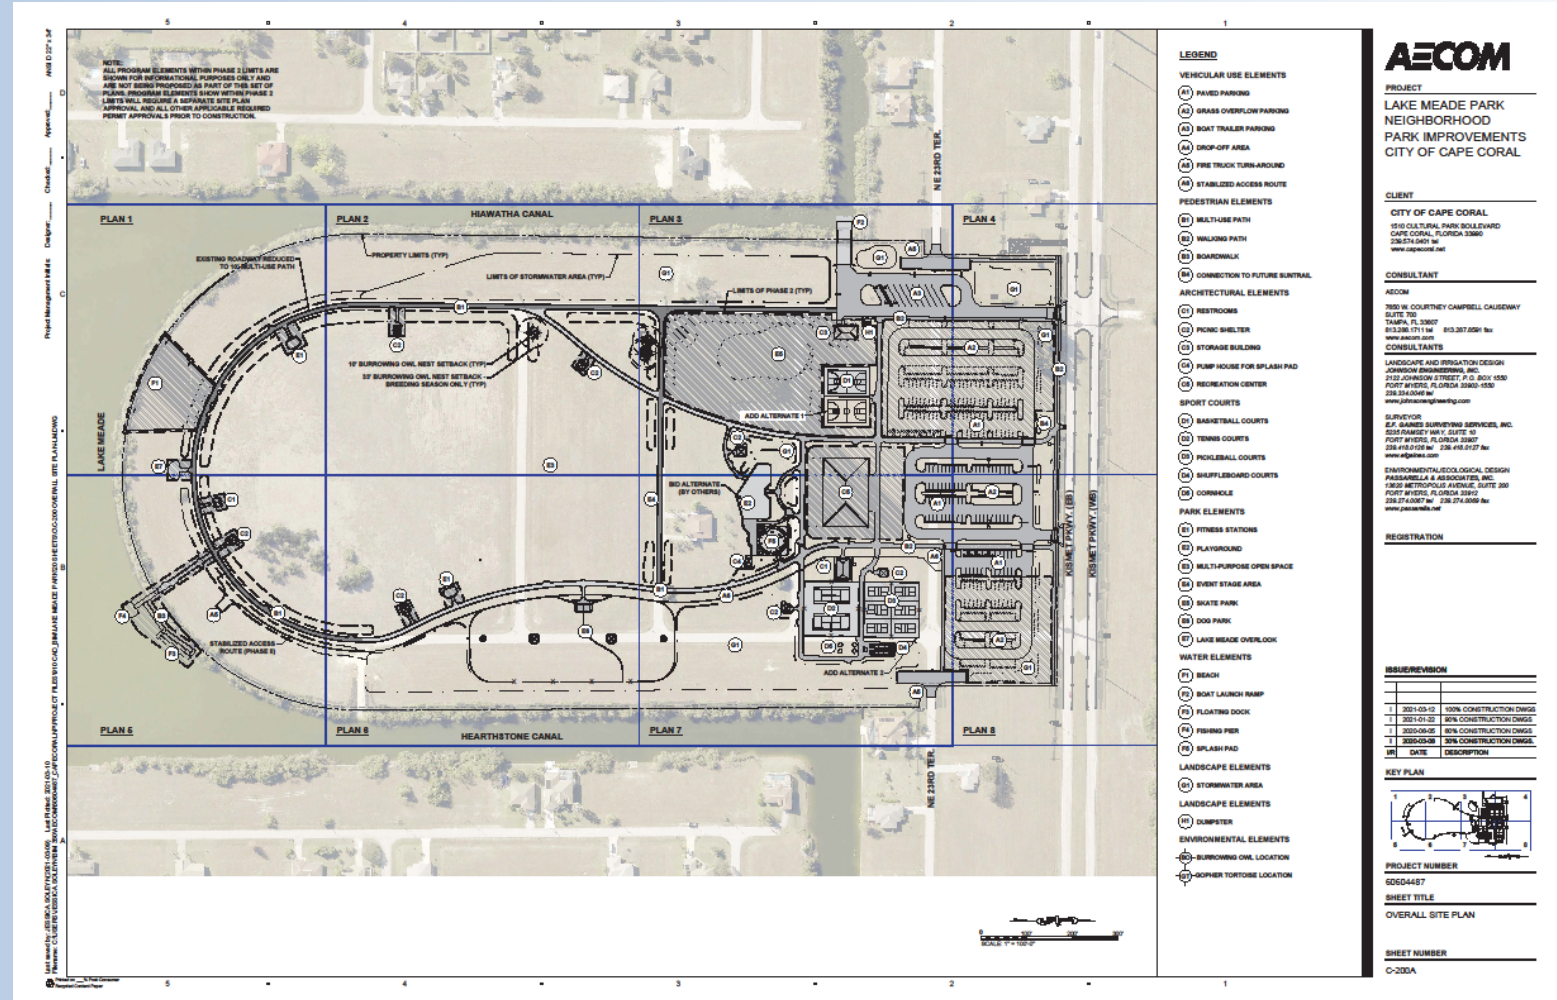

Yacht Club

- **Construction Manager:**
Wright Construction
- **Waiting on ACOE and DEP Permits**
- **GMP bidding on hold**
- **Contract Duration:**
Estimate 2 Years



THANK YOU

Any Questions?

